




CITY OF WICHITA FALLS TRANSPORTATION PROJECTS FY 2017-2018

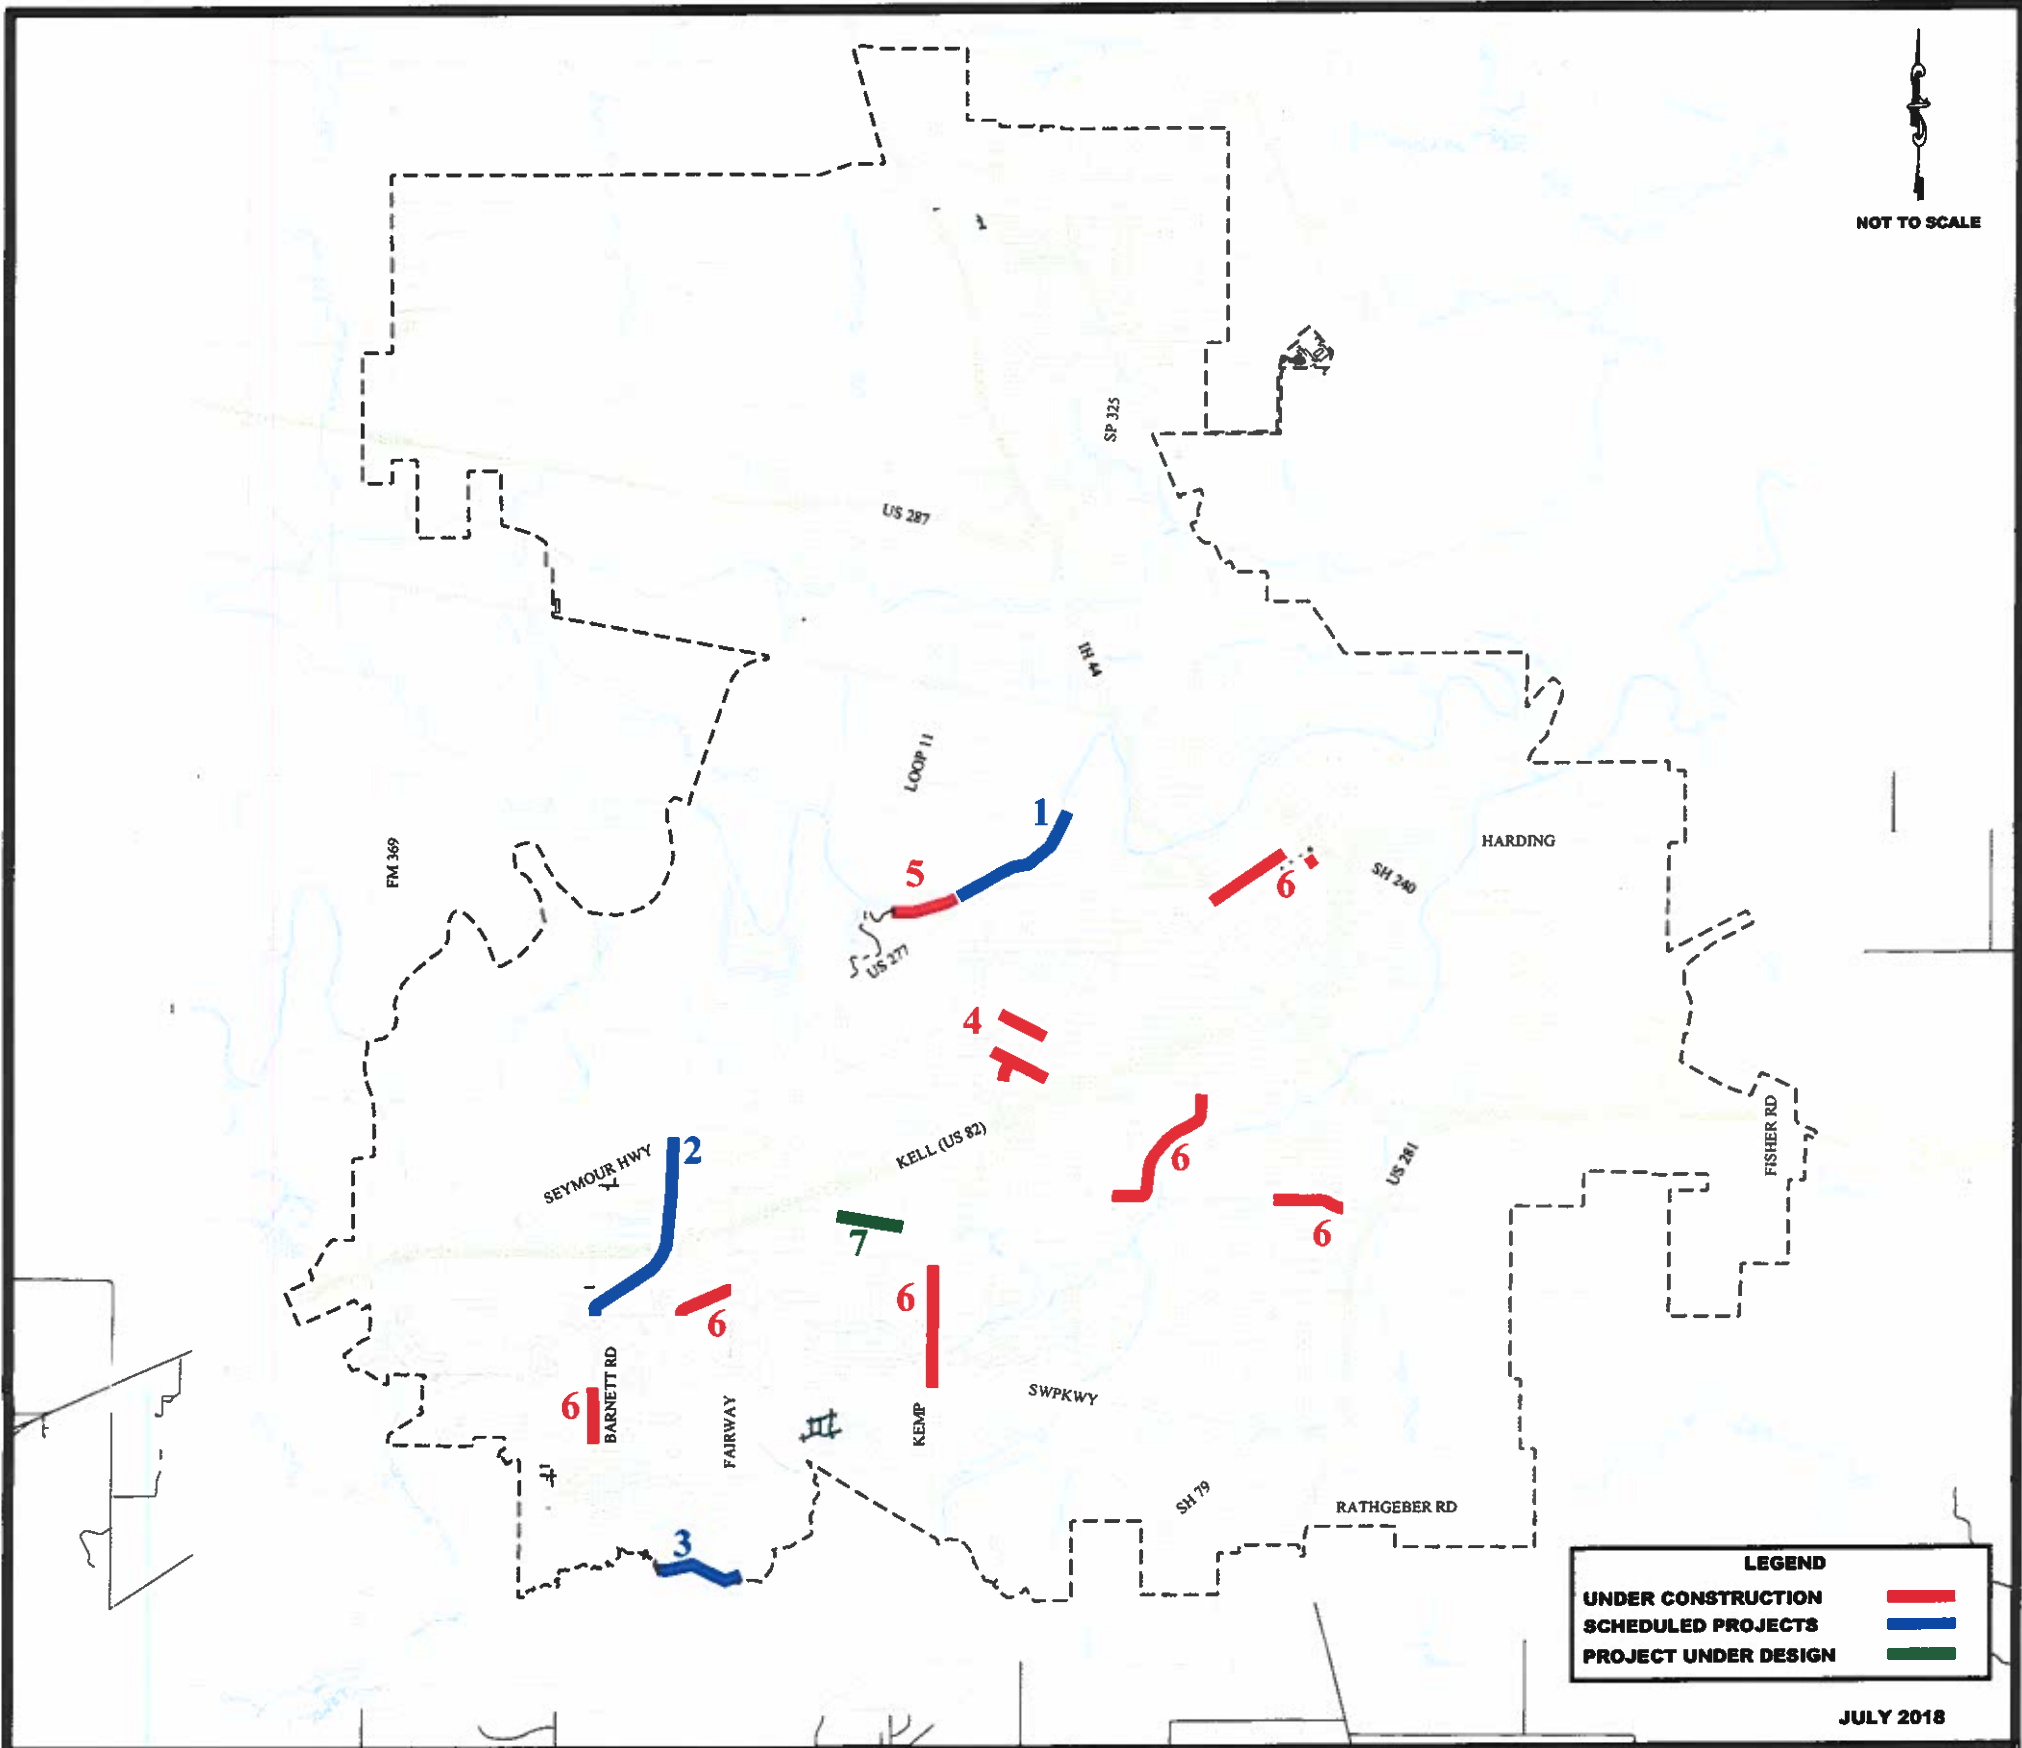

LEGEND	
UNDER CONSTRUCTION	—
SCHEDULED PROJECTS	—
PROJECT UNDER DESIGN	—

JULY 2018

CITY OF WICHITA FALLS FY 2017-2018 TRANSPORTATION PROJECTS

PROJECT	LIMITS	PROJECT DESCRIPTION	PROPOSED AWARD DATE	ESTIMATED COST
SCHEDULED PROJECTS				
1	Trail Along Wichita River From Loop 11 to Lucy Park	Construct Hike and Bike Trail	April 2019 100% design	\$2,251,735
	TA Set-Aside Funding			
2	Trail Along BNSF RR From Barnett Rd to Seymour Hwy	Construct Hike and Bike Trail	Oct 2019 80% design	\$2,124,440
	TA Set-Aside Funding			
3	Trail Along Lake Wichita West of Lake Wichita Park	Construct Hike and Bike Trail	Sept 2020 0% design	\$1,528,750
	TA Set-Aside Funding			
UNDER CONSTRUCTION				
4	2018 Kemp-Monroe Drainage Project Phase 2 Ave L and Ave I	Construct Drainage System	May 5, 2018 0% Complete MH Civil	\$4,112,000
5	Wichita Bluff Hike and Bike Trail Phase 2 Wichita Bluff to Loop 11	Construct Hike and Bike Trail	3-28-2017 40% Complete Scales Construction	\$1,436,123
	Tap Funding			
6	2018 Asphalt St Rehab Rehabilitation Project Various Streets	Base Repair Mill and Overlay	3-20-2018 50% Complete Foutsco Paving Co.	\$1,813,080
PROJECTS UNDER DESIGN AWAITING FUTURE FUNDING				
7	Maplewood Extension From McNeil Ave to Lawrence Rd	Construct New Road	50% design	\$1,880,000
